Project Planning Phase

Import Data using Transform Maps (Spreadsheet)

1. Planning Overview

This plan divides the project into eight phases over eight weeks with clear ownership among the five team members.

2. Work Breakdown Structure

Phase	Key Tasks	Owner	Duration
1 Brainstorming	Ideation, mind map, empathy map	All	Week 1
2 Requirements	Functional / non-functional requirements	Member 2	Weeks 1-2
3 Design	Data model, transform design, architecture	Member 3	Weeks 2-3
4 Planning	Schedule, roles, risk plan	Member 1	Weeks 2-3
5 Development	Table, Import Set, Transform Map, coalesce, reports	Members 1, 2, 3, 5	Weeks 3-5
6 Testing	Test cases, execution, defect log	Member 4	Weeks 5-6
7 Documentation	User guide, report, README	Member 5	Weeks 5-7
8 Demonstration	Demo video, presentation	All	Weeks 7-8

3.Project Timeline

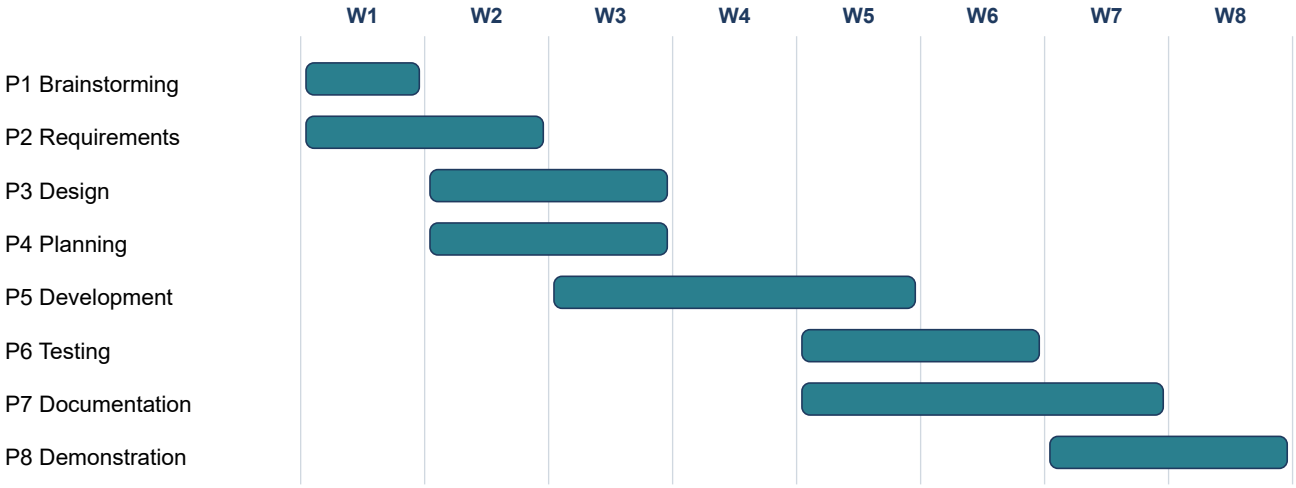


Figure 1: Project timeline (weeks)

4.Team Roles

Member	Name	Role	Responsibility
Member 1	Sornajothika KT	Team Lead / ServiceNow Developer	Custom table creation, overall coordination, GitHub repository management
Member 2	Reshma L	Data Preparation Analyst	Spreadsheet design, sample data creation, Import Set loading
Member 3	Sharmila J	Transform Map Developer	Transform Map, field mapping, coalesce configuration
Member 4	Shridevi M	Test Engineer	Test case design, execution, defect reporting, Transform History validation
Member 5	Suwetha R	Documentation & Reporting Lead	Reports/dashboards, documentation, demonstration video and presentation

5.Risk Management

Risk	Impact	Mitigation
Incorrect field mapping	Wrong data in target table	Verify mapping in Mapping Assist before transform
Duplicate records on re-import	Data inconsistency	Enable Coalesce on Employee ID
Instance downtime / hibernation	Schedule delay	Wake PDI early; keep backups of spreadsheet
Member unavailability	Task delay	Cross-training and shared GitHub repository

6.Communication and Version Control

- Daily short stand-up on the team group chat.
- All deliverables uploaded to the public GitHub repository, phase-wise.
- Each member commits with a meaningful message; Member 1 reviews merges.
